SUMMARY OF UNCONFINED COMPRESSION TEST RESULTS
NECHES RIVER SALT WATER BARRIER
BEAUMONT, TEXAS
TABLE-

BORING NO.	DEPTH (FT.)	DENSITY DATA Moisture Cont. %	DENSITY DATA Dry Wt (pcf)	MECHANICAL ANALYSIS Gvl.	MECHANICAL ANALYSIS Sand	MECHANICAL ANALYSIS Fine	ATTERBURG LIMITS L.L.	ATTERBURG LIMITS P.L.	% STRAIN @ MAX. STRESS	UNCON. COMP. STR (pcf)	CLASSIFICATION
98-21	24-26	18.2	106.6	0	18	82	24.0	13.0	3.9	630	Sandy Clay, Medium stiff, Gray
98-21	30-32	18.9	105.0	0	16	84	32.0	16.0	4.6	2090	Sandy Clay, Very stiff, Gray & yellowish gray
98-22	24-26	16.9	110.0	0	16	84	31.0	16.0	6	1980	Silty Clay, W / silt & sand seams,Very stiff, Gray & yellowish gray
98-23	16-18	27.9	84.9	0	14	86	47.0	24.0	4.3	1270	Silty Clay, W / sand seams & sand pockets, Stiff, Gray
98-24	10-12	41.7	77.8	0	1	99	134.0	47.0	3.6	90	Clay, W / decayed wood & roots, Very soft, Gray
98-24	28-30	14.7	114.1	0	8	92	25.0	14.0	10.5	2170	Silty Clay, W / sand seams, Very stiff, Gray
98-24	44.5-46	17.0	107.0	0	12	88	39.0	18.0	7.5	2000	Silty Clay, W / sand seams, Very stiff, Red & Gray
98-25	32-34	19.0	104.8	-	-	-	65.0	24.0	3.2	2220	Clay, W / calc nod & fer stains, slks, Very stiff, Brown & gray
98-25	40-42	15.3	111.4	-	-	-	-	-	3.4	3660	Clay, W / calc nod, fer stains, & sd sms, Very stiff, Reddish brown & gray
98-26	25-27	19.5	104.4	0	2	98	25.0	15.0	5	560	Silty Clay, W / sand seams, Medium stiff, Gray
98-26	35-37	16.8	106.6	0	7	93	41.0	18.0	4	2010	Silty Clay, W / sand seams, stiff, Gray
98-35	6.5-8	17.5	111.7	-	-	-	33.0	17.0	6.8	1370	Silty Clay, Stiff, Gray
98-40	14-16	76.4	43.9	-	-	-	-	-	2.1	70	Clay, W / decayed wood roots & organic material, Very soft, Gray
98-40	22-24	20.5	102.2	0	3	97	47.0	20.0	3.6	2030	Silty Clay, W / sand seams, Very stiff, Olive gray
98-40	32-34	25.5	94.5	-	-	-	-	-	3.3	2190	Clay, W / fer stains, slks,Very stiff, Reddish brown & gray
98-42	14-16	37.6	81.0	0	4	95	63.0	25.0	2.5	1060	Clay, W / fer nod & fer stains, Stiff,Yellowish brown

DESIGN FILE: DGNSPECIFICATION$$ CREATED BY: $$$$ ON: $$$DATE$$$$ AT: $TIME

DIRECT SHEAR STRENGTH				
BORING NO.	SAMPLE NO.	DEPTH (FT.)	ϕ (DEGREES)	LINE NO.
98-39	19	36-38	21.9	1
		50-52	19.8	2
98-33	13	35-37	26.6	3
	19	47-49	19.8	4
98-31	10	32-34	18.2	5
	15	42-44	25.2	6
98-30	17	34-36	25.7	7
	24	48-50	23.7	8
98-33		50-52	17.5	9
98-34		35-37	15.7	10

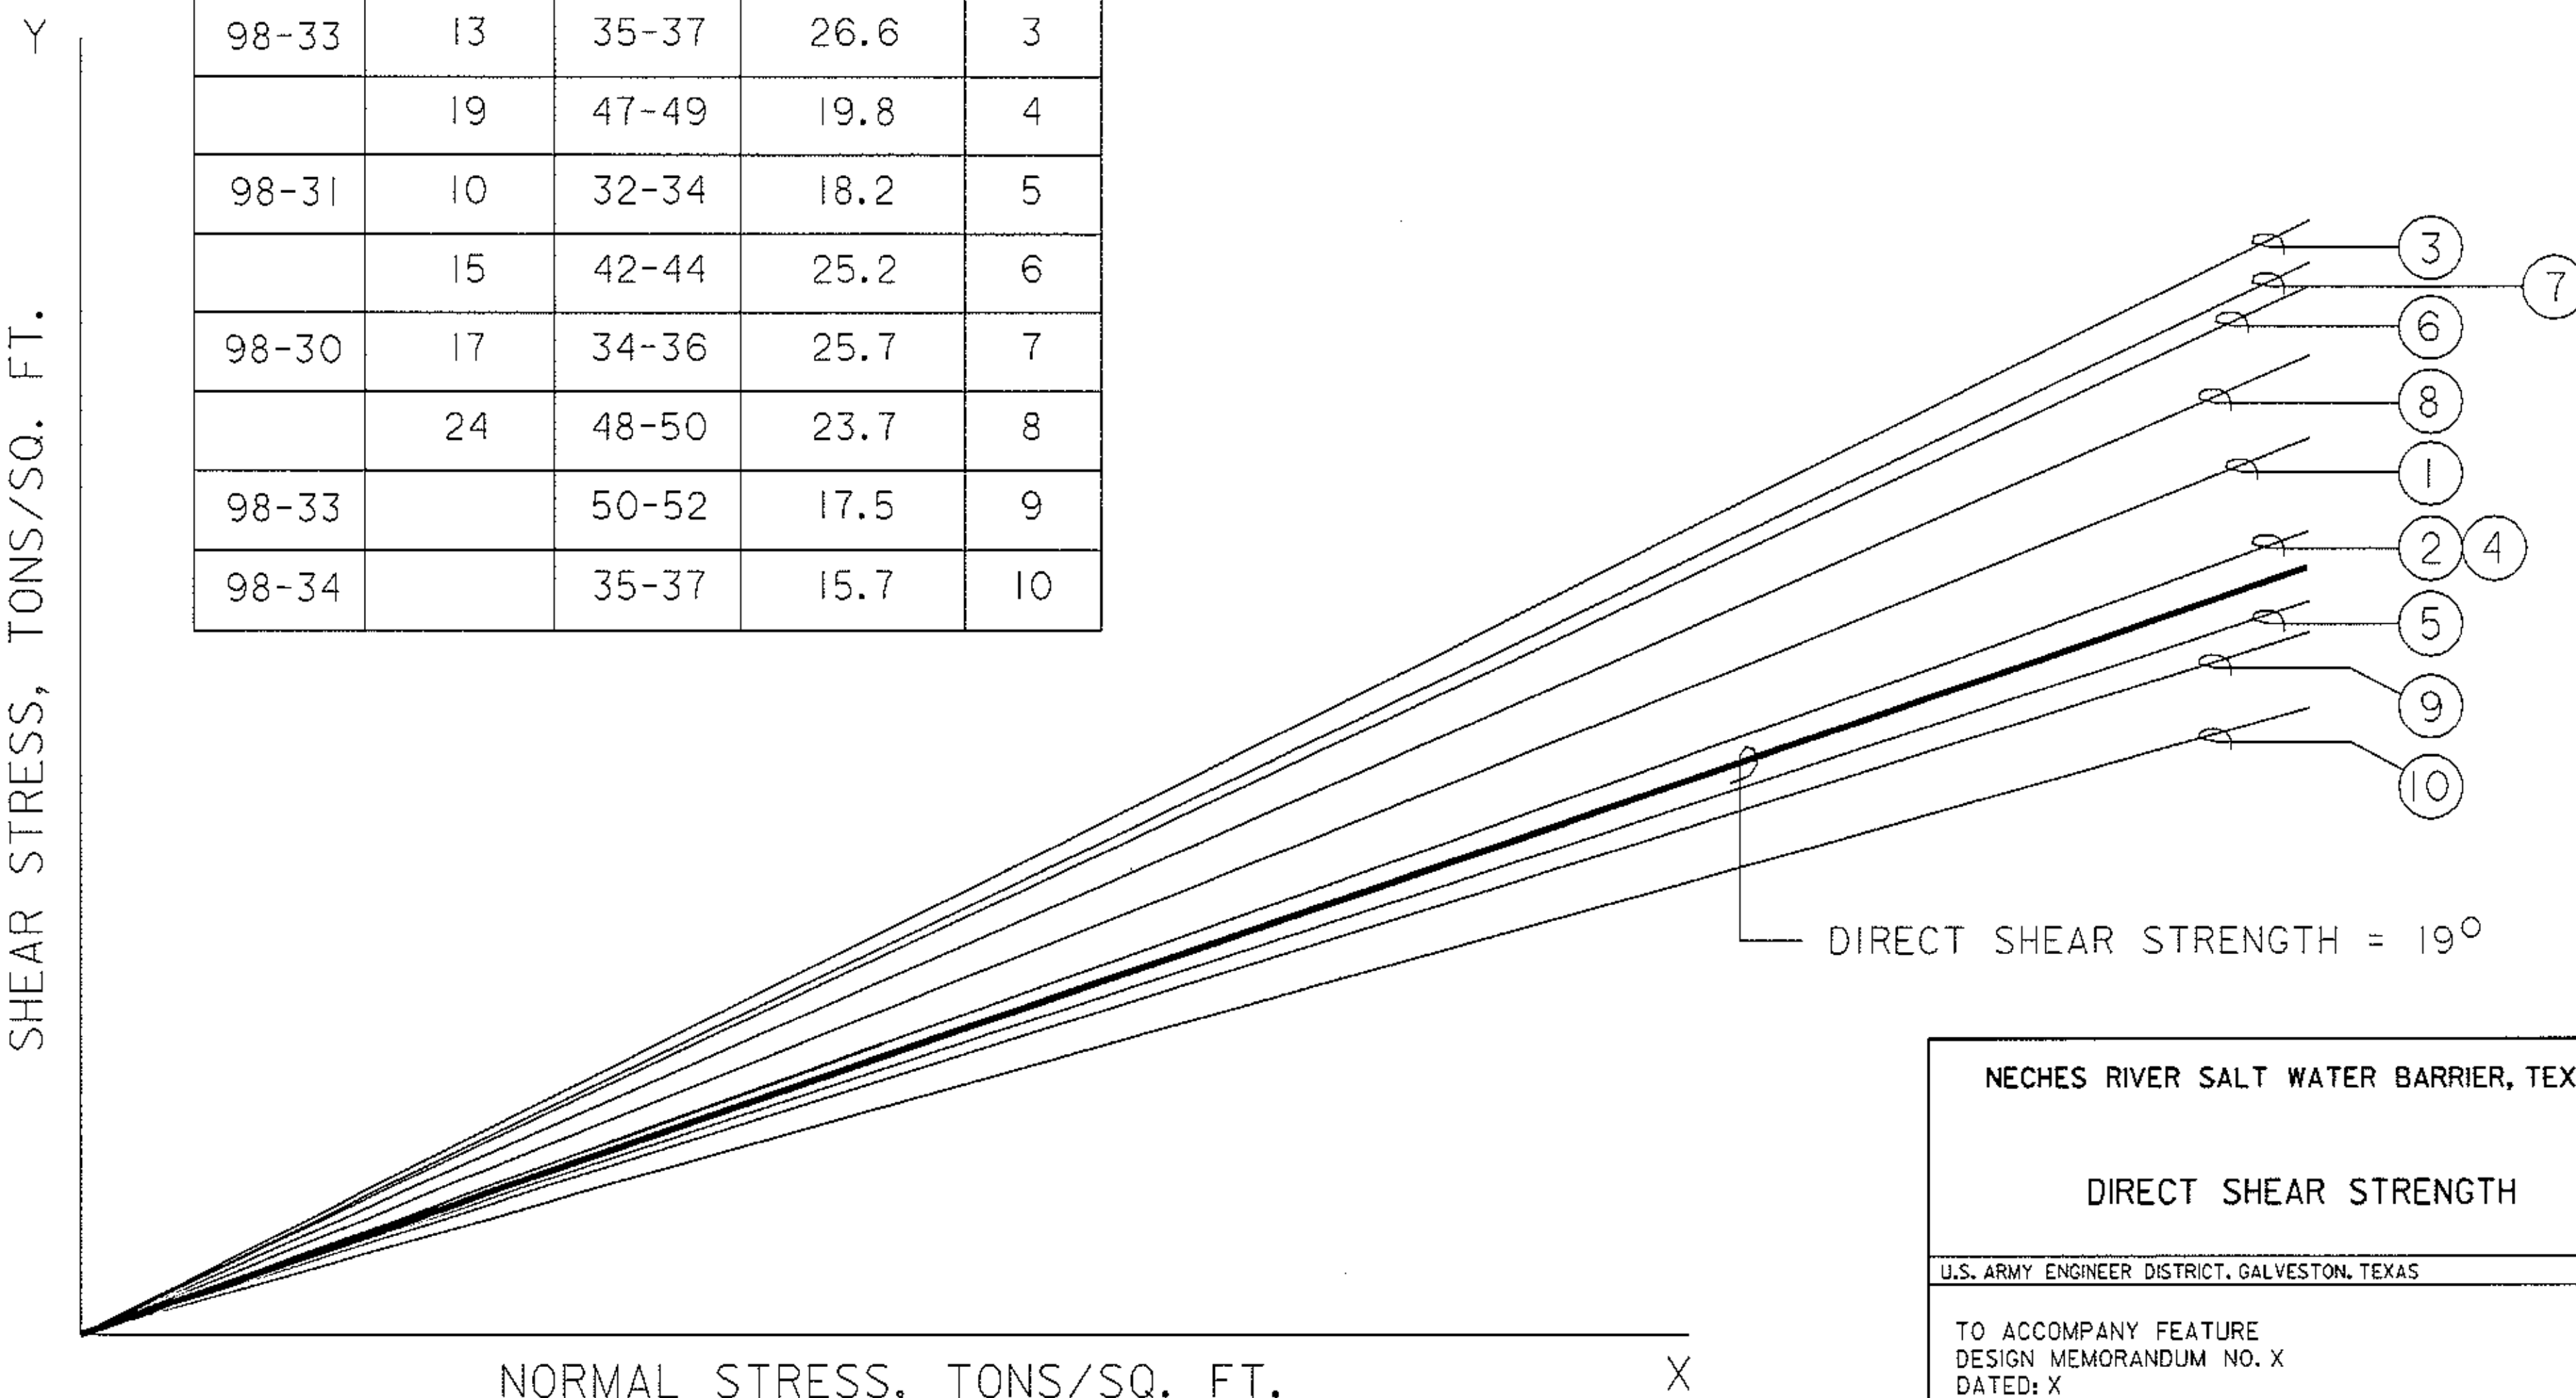

NECHES RIVER SALT WATER BARRIER, TEXAS

DIRECT SHEAR STRENGTH

U.S. ARMY ENGINEER DISTRICT, GALVESTON, TEXAS

TO ACCOMPANY FEATURE
DESIGN MEMORANDUM NO. X
DATED: X

EXHIBIT

k:\user\p_norm\netch\shear.dgn Apr. 06, 1999 13:06:20

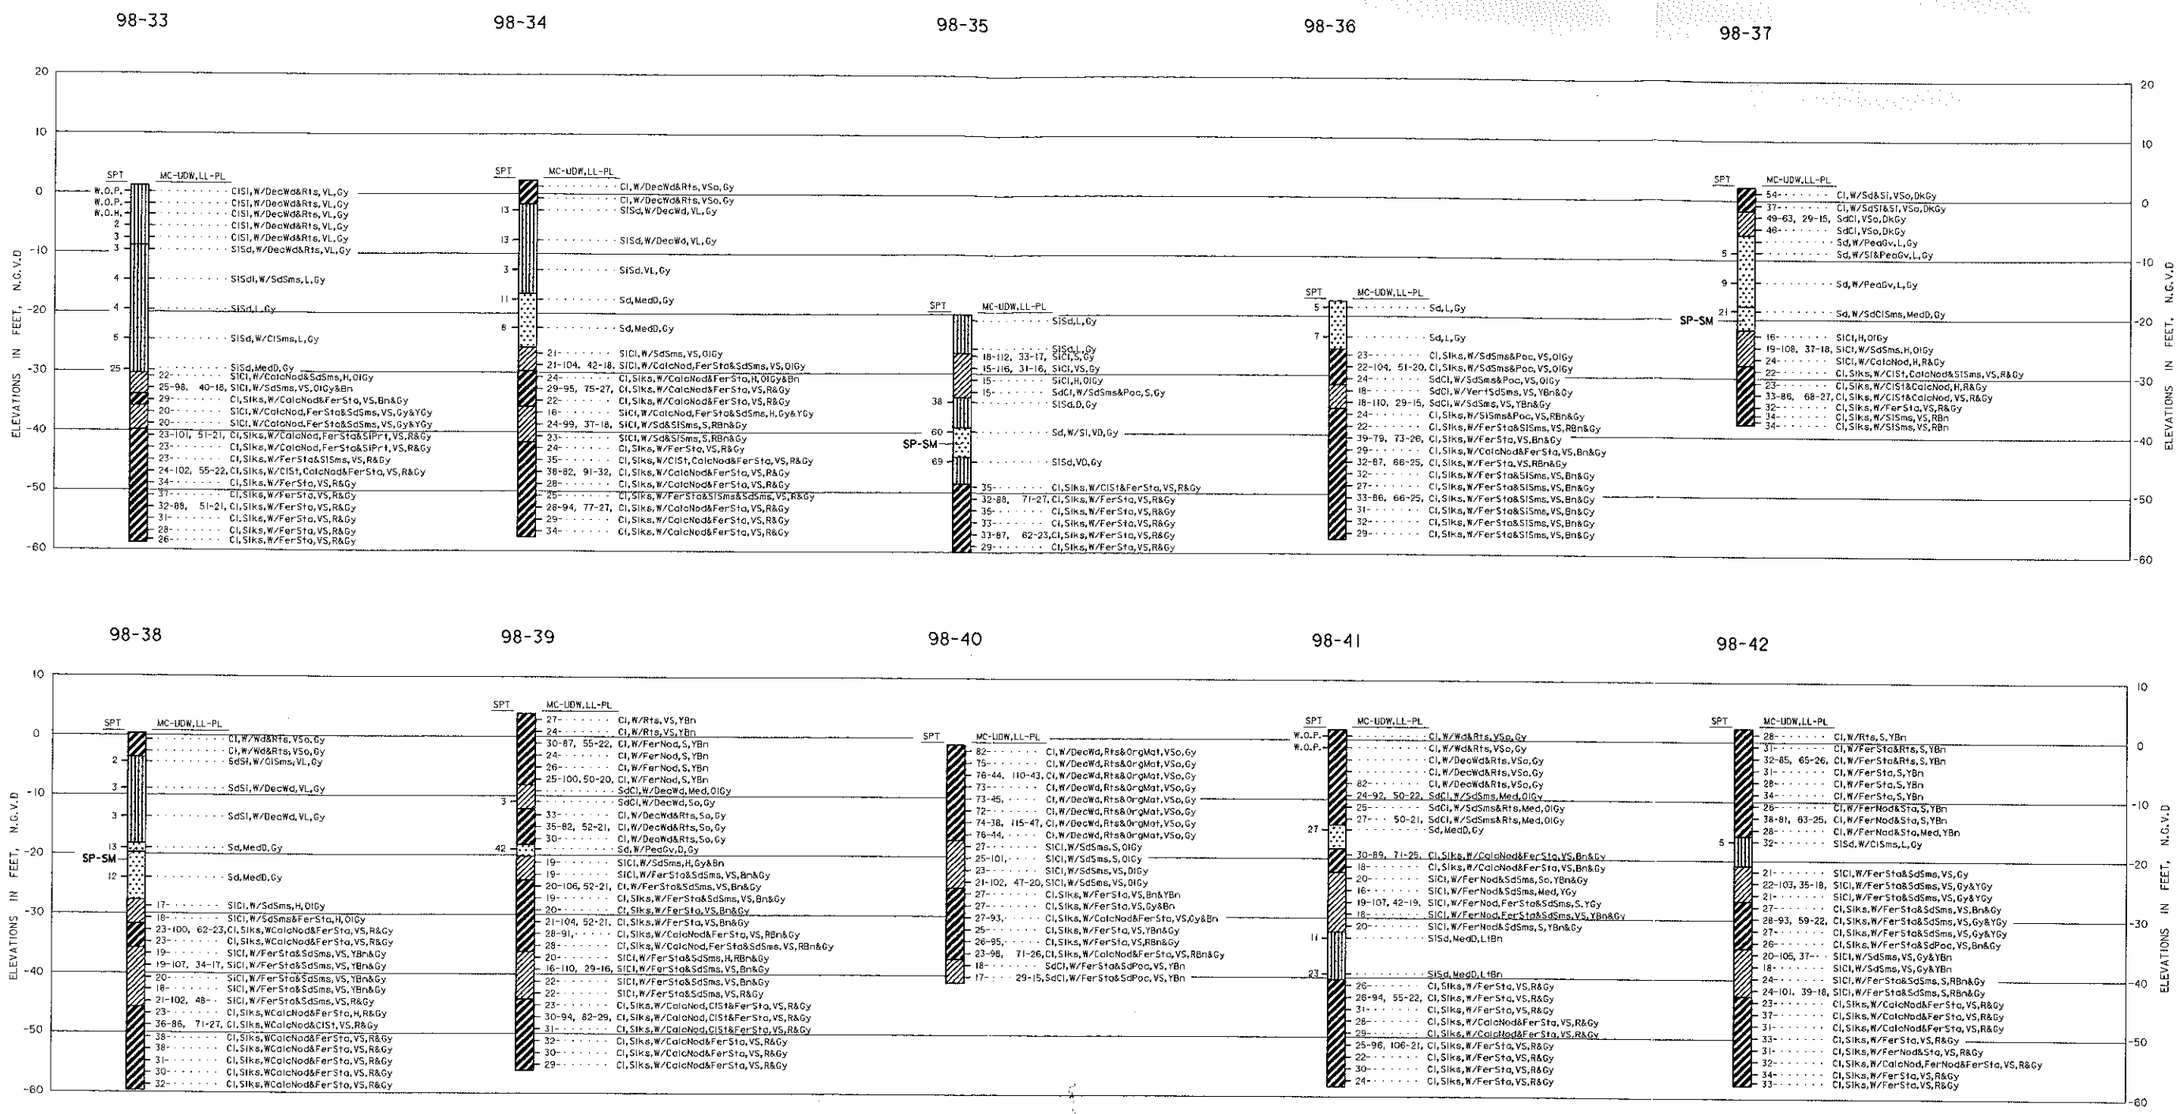

NOTES;

1. SOILS HAVE BEEN CLASSIFIED IN ACCORDANCE WITH ASTM 2487-93 "CLASSIFICATION OF SOILS FOR ENGINEERING PURPOSES (UNIFIED SOILS CLASSIFICATION SYSTEM)". CONSISTENCY OF SOILS SUCH AS SOFT, MEDIUM, HARD, LOOSE, DENSE, ETC., ARE RELATIVE TERMS BASED ON ESTIMATED UNDISTURBED SHEAR STRENGTH OF THE MATERIAL AS DETERMINED BY VISUAL CLASSIFICATION POCKET PENETROMETER TESTS AND PENETRATION RESISTANCE DURING SAMPLING.
2. FIGURES TO THE RIGHT OF BORING LOGS ARE WATER CONTENTS IN PERCENT OF THE DRY WEIGHT, DRY DENSITY, LIQUID LIMIT, PLASTIC LIMIT, AND BAR LINEAR SHRINKAGE. (MC-UDW),(LL-PL),(B.L.S.)* FIGURES TO THE LEFT OF BORING LOGS ARE BLOWS PER FOOT OF PENETRATION FROM STANDARD PENETRATION TESTING.
3. BORINGS WERE DRILLED USING WET ROTARY DRILLING TECHNIQUES AND UNDISTURBED SAMPLES WERE RECOVERED WITH A 3-INCH DIAMETER THIN WALL SAMPLER WHERE COHESIVE MATERIALS WERE ENCOUNTERED.WHERE COHESIONLESS MATERIALS WERE ENCOUNTERED, DISTURBED SAMPLES WERE TAKEN WITH A SPLIT SPOON SAMPLER DURING PERFORMANCE OF STANDARD PENETRATION TESTING.
4. WATER TABLE LEVELS SHOWN ON BORING LOGS WERE DETERMINED AFTER DRILLING BORINGS BY MEASURING THE TOP OF FLUID LEVELS IN THE BORINGS. INASMUCH AS WET ROTARY DRILLING TECHNIQUES AND DRILLING MUD WERE USED TO DRILL THE HOLES, THE LEVEL OF DRILLING FLUIDS IN THE BORE HOLES MAY NOT HAVE STABILIZED TO THE LEVEL OF THE ACTUAL WATER TABLE. ADDITIONALLY, WATER TABLES IN THE FIELD ARE LIKELY TO FLUCTUATE DEPENDING ON WEATHER CONDITIONS. THEREFORE, SOME VARIATION SHOULD BE ANTICIPATED BETWEEN WATER TABLES INDICATED AND WATER TABLES ENCOUNTERED IN THE FIELD.

VISUAL CLASSIFICATIONS:

Blk Blackey	Org Organic	Wd Wood(en)
Bn Brown(ish)	Ol Olive	W/ With
Calc Calcareous	Pea Pea	W.O.H.
Cl Clay(ey)	Poc Pockets	W.O.P.
D Dense	R Red(dish)	Y Yellow(ish)
Dec Decay(ed)	Rts Root(s)	
Dk Dark	S Stiff	
Gv Gravel(ly)	Sd Sand(y)	
Gy Gray(ish)	Sh Shell(y)	
H Hard	Sl Silty	
L Loose	Sms Seams	
Ly Layer(s)	So Soft	
Lt Light	St Stone(s)	
Mat Material	Str Structure	
Med Medium	V Very	
Nod Nodules	Vert Vertical	

LABORATORY CLASSIFICATIONS:

CH INORGANIC CLAYS OF HIGH PLASTICITY, FAT CLAYS.

CL INORGANIC CLAYS OF LOW TO MEDIUM PLASTICITY, LEAN CLAYS.

ML INORGANIC SILTS AND VERY FINE SANDS, WITH SLIGHT PLASTICITY.

SC CLAYEY SANDS, SAND-CLAY MIXTURES.

SM SILTY SANDS, SAND-SILT MIXTURES.

SP POORLY GRADED SANDS OR GRAVELLY SANDS, LITTLE OR NO FINES.

NOTES:
SEE PLATE _____ FOR BORING LOCATIONS.
SEE PLATE _____ FOR BORING NOTES AND LEGEND.

REVISION	DATE	DESCRIPTION	BY

OFFICE OF THE DISTRICT ENGINEER
U.S. ARMY ENGINEER DISTRICT, GALVESTON
CORPS OF ENGINEERS
GALVESTON, TEXAS

DRAWN BY: * P.N.
DESIGNED BY: * P.N.
CHECKED BY: * I.S.
SUBMITTED BY: *
CHIEF,
APPROVED: *
CHIEF,
APPROVED: *
CHIEF, ENGINEERING DIVISION
DATE: X
* AS REQUIRED BY ENGINEER REGULATION NO. 1110-1-8021

NECHES RIVER SALT WATER BARRIER, TEXAS
X
X
LOGS OF BORINGS
X

SCALE: AS SHEET
SPEC. DATE:
DRAWING NUMBER: X
SHEET X OF X FILE NO. X

Prepared under the direction of Nicholas J. Buechler, Lt. Col. (P), C.E., District Engineer

EXHIBIT

DESIGN FILE: #DOMSPECIFICATIONS
CREATED BY: #USERNAME#
DWG: #MONTH#DAY#
PTS: #TIME#

..\user\p_norm\netch\bore3_98.dgn Apr. 06, 1999 12:54:25

U.S. ARMY CORPS OF ENGINEERS
GEOTECHNICAL BORING DATA

PROJECT NAME Neches River Salt water Barrier

LOG OF BORING NO. 98-35

LOCATION/STATION X = 3543945.29 , Y = 876459.74

DATE/TIME STARTED 4-15-98 5:10
DATE/TIME COMPLETED 4-15-98 / 7:59 PM

TIDE ELEVATION 2.8 MLT DATUM, TIME 5:10 LOCATION LT. BKN.#

WATER DEPTH 19.5

DEPTH FROM WATER SURFACE
TO BOTTOM OF BORING 59.5

WEATHER cloudy

DRILL RIG MANUFACTURE
MODEL NO. Failling 36

DRILLER Dempsey Graves
LOGGER Fraj Mostamand

DRILLER'S/LOGGER'S COMMENTS

pc.well.con.log.r

U.S. ARMY CORPS OF ENGINEERS

BORING NO. 98-35 DATE: BEGIN 4-15-98 PAGE 2 13
JOB NO. 1140086148 COMPLETE 4-15-98 Thin Walled Tube
PROJECT Neches River Salt water Barrier ■ 3" □ 6"
LOCATION X=3543945.29, Y=876459.74
ELEVATION OF HOLE
MANUFACTURER'S DESIGNATION OF DRILL RIG Failing 36
[redacted] WATER: DEPTH 19.5 ft., ELEV. ____ ft., at end of Drilling
WEATHER Cloudy
DRILLER Dempsey Geaves LOGGER Iraj Mostamand

Mud line

DEPTH, FEET	SAMPLE	SAMPLE NO.	PEN./TORVANE SPT.-BLOW COUNT	COLOR	MATERIAL TYPE	CONSISTENCY	SECONDARY CONSTITUENTS	STRUCTURAL FEATURES AND COMMENTS
0	X	1	2 2 2	Gray	Sand	Loose	Silty	- Set 26' of 4"Ø casing (Total casing below Mud 4'
5	X	2	1 2 2	Gray	Sand	Loose	Silty	sic 26'
		3	2.00	Gray	Clay	V.stiff	Silty	- Set
		4	3.75	olive gray	Clay	V.stiff	Silty	
10		5	4.25	olive gray	Clay	Hard	Silty	- Set 10' of casing Total 36' Total casing below Mudline 12'
		6	1.00	Gray	Clay	Stiff	Sandy	- w/ Sa sms & Sa pkts so @ bottom of sample
15	X	7	6 15 23	Gray	Sand	Dense	Silty	
20	X	8	12 23 37	Gray	Sand	V. Dense	Silty	
25	X	9	10 27 42	Gray	Sand	V. Dense	Silty	el @ 28.5
30		10	3.5	Red & gray	Clay	V. stiff		- w/ Clay stone, Fest, SLS
		11	3.50	Red & gray	Clay	V. stiff		- w/ Fest, SLS
		12	3.50	Red & gray	Clay	V. stiff		- w/ Fest, SLS
35		13	3.50	Red & gray	Clay	V. stiff		- w/ Fest, SLS

U.S. ARMY CORPS OF ENGINEERS

BORING NO. 98-35 DATE: BEGIN 4-15-98 PAGE 3 / 3

JOB NO. 1140086148 COMPLETE 4-15-98 Thin Walled Tube

PROJECT Neches River Salt water Barrier ■ 3" □ 6"

LOCATION X = 3543945.29, Y = 876459.74

ELEVATION OF HOLE

MANUFACTURER'S DESIGNATION OF DRILL RIG Failing 36

[redacted] WATER: DEPTH 19.5 ft., ELEV. ____ ft., at end of Drilling

WEATHER Cloudy

DRILLER Dempsey Scares LOGGER Troy Mostamand

DEPTH, FEET	SAMPLE	SAMPLE NO.	PEN./TORVANE SPT.-BLOW COUNT	COLOR	MATERIAL TYPE	CONSIS-TENCY	SECONDARY CONSTITUENTS	STRUCTURAL FEATURES AND COMMENTS
35								
		14	3.50	Red & gray	Clay	V. stiff		- w/ Fest, SLS
		15	3.50	Red & gray	Clay	V. stiff		- w/ Fest, SLS
40								
45								
50								
55								
60								
65								
70								

GEOTEST ENGINEERING, INC.
