U.S. ARMY CORPS OF ENGINEERS

BORING NO. 98-98 DATE: BEGIN 12-1-98 PAGE 1 / 1
JOB NO. 1140114801 COMPLETE 12-1-98 Thin Walled Tube
PROJECT Placement Areas NO. 6C and 6D ■ 3" ☐ 6"
LOCATION See plan of Borings
ELEVATION OF HOLE
MANUFACTURER'S DESIGNATION OF DRILL RIG Marsh Buggy F36
GROUNDWATER: DEPTH Dry ft., ELEV. ____ ft., at end of Drilling
WEATHER Cloudy
DRILLER Dempsey Gearen LOGGER Iraj Mostamand

DEPTH, FEET	SAMPLE	SAMPLE NO.	PEN./TORVANE SPT.-BLOW COUNT	COLOR	MATERIAL TYPE	CONSISTENCY	SECONDARY CONSTITUENTS	STRUCTURAL FEATURES AND COMMENTS
0		1	0.50	DK. gray	Clay	M. stiff		-w/roots
		2	0.50	DK. gray	Clay	M. stiff		-w/roots
5'		3	0.50	DK. gray	Clay	M. stiff		
		4	4.50+	Yellowish Brown	Clay	Hard	silty	-w/calc nod & Fer stains
		5	4.5+	Yellowish Brown	Clay	Hard	silty	-w/calc nod & Fer stains
10		6	3.75	Yellowish Brown	Clay	V. stiff	silty	-w/calc nod & Fer stains
		7	3.25	Yellowish Brown	Clay	V. stiff		-w/calc nod, Fer stains & silt sms
15		8	3.25	Yellowish Brown	Clay	V. stiff		-w/calc nod, Fer stains, SLKS
		9	3.25	Yellowish Brown	Clay	V. stiff		-w/calc nod, Fer stains, SLKS
		10	3.50	Yellowish Brown	Clay	V. stiff		-w/calc nod & Fer stains, SLKS
20		11	3.25	Yellowish Brown	Clay	V. stiff		-w/calc nod & Fer stains, SLKS
		12	4.00	Yellowish Brown	Clay	V. stiff		-w/calc nod & Fer stains, SLKS
25		13	4.25	Yellowish Brown	Clay	Hard		-w/calc nod & Fer stains, SLKS
								Dry after drilling
30								
35								

GEOTEST ENGINEERING, INC.

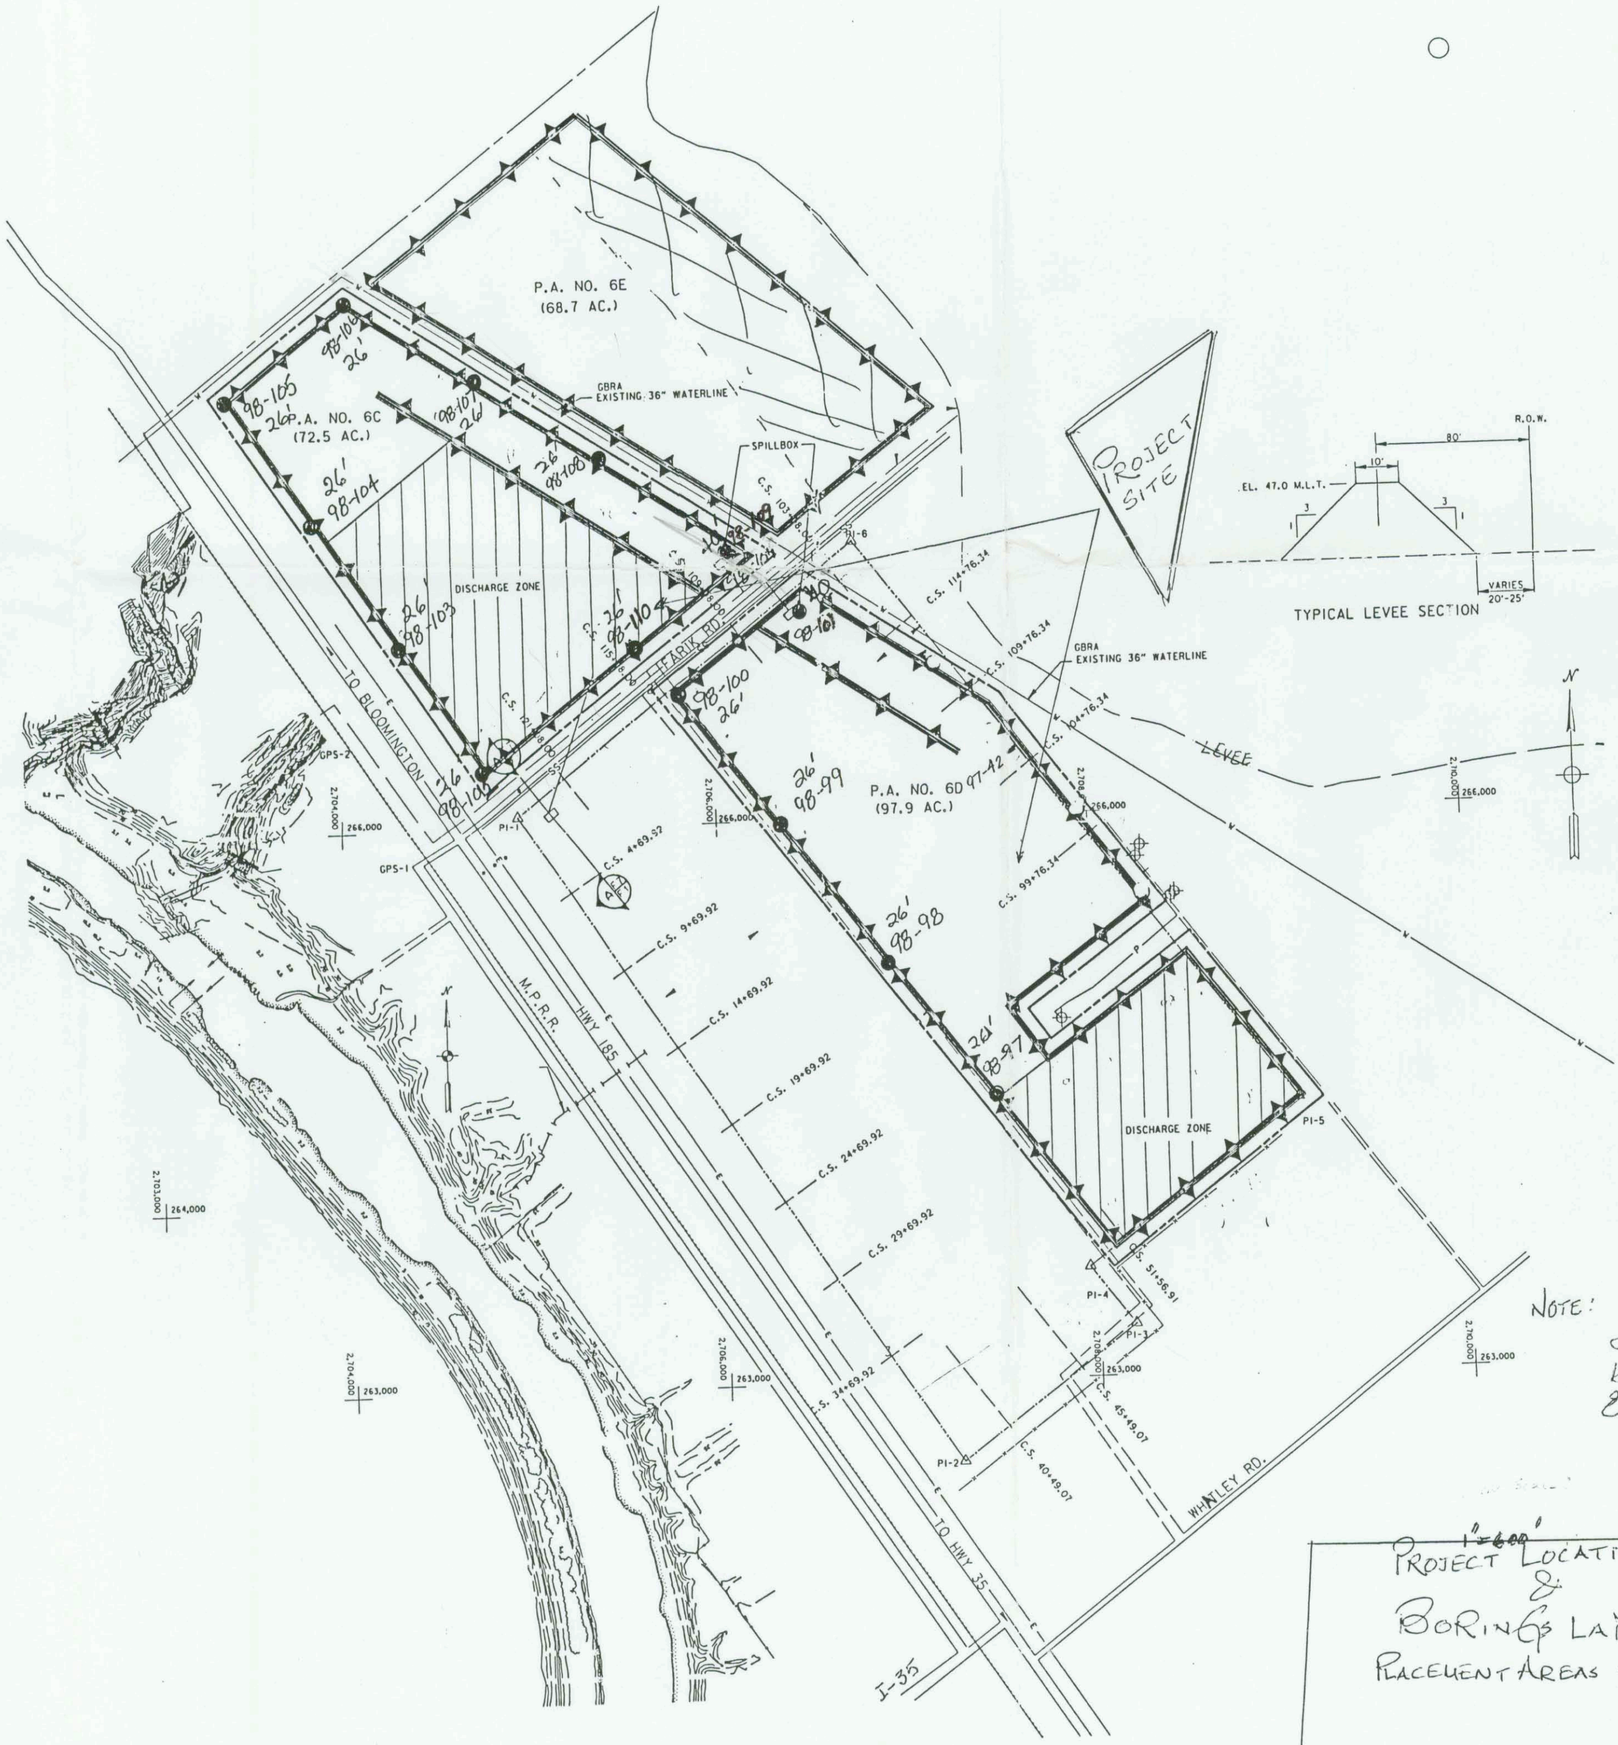

NOTE: All the borings shall be drilled to a depth 26' fee below the ground line EXCEPT Borings 98-101 & 98-109 shall be 40' fee deep.

1"=600'

PROJECT LOCATION MAP
&
BORING LAYOUT
PLACEMENT AREAS 6C & 6D.

FIG: 3
