U.S. ARMY CORPS OF ENGINEERS

BORING NO. 98-104 DATE: BEGIN 12-3-98 PAGE 1 / 1
JOB NO. 1140114801 COMPLETE 12-3-98 Thin Walled Tube
PROJECT Placement Areas NO. 6C and 6D ■ 3" □ 6"
LOCATION See plan of Borings
ELEVATION OF HOLE
MANUFACTURER'S DESIGNATION OF DRILL RIG Marsh Buggy - F36
GROUNDWATER: DEPTH Dry ft., ELEV. ____ ft., at end of Drilling
WEATHER Clear
DRILLER Dempsey Gearen LOGGER Jay Mostamand

DEPTH, FEET	SAMPLE	SAMPLE NO.	PEN./TORVANE SPT.-BLOW COUNT	COLOR	MATERIAL TYPE	CONSISTENCY	SECONDARY CONSTITUENTS	STRUCTURAL FEATURES AND COMMENTS
0		1	0.50	DK. gray	Clay	M. stiff		-w/roots
		2	0.75	Gray	Clay	M. stiff		-w/calc nod
5		3	1.25	Gray	Clay	stiff		-w/calc nod
		4	4.5+	Yellowish Brown	Clay	Hard		-w/calc nod, Fer stains, SLKS
		5	4.5+	Yellowish Brown	Clay	Hard		-w/calc nod, Fer stains, SLKS
10		6	4.5+	Yellowish Brown	Clay	Hard		-w/calc nod, Fer stains, SLKS
		7	3.25	Yellowish Brown	Clay	V. stiff		-w/calc nod, Fer stains, SLKS
15		8	2.75	Yellowish Brown	Clay	V. stiff		-w/calc nod & Fer stains, SLKS
		9	2.75	Yellowish Brown	Clay	V. stiff		-w/calc nod & Fer stains, SLKS
		10	3.25	Yellowish Brown	Clay	V. stiff		-w/Fer stains, SLKS
20		11	4.5+	Yellowish Brown	Clay	Hard		-w/Fer stains, SLKS
		12		Yellowish Brown	Silt	M. Dense		
25		13	2.75	Yellowish Brown	Clay	V. stiff		-w/silt layer, Fe stains, SLKS
30								
35								

GEOTEST ENGINEERING, INC.

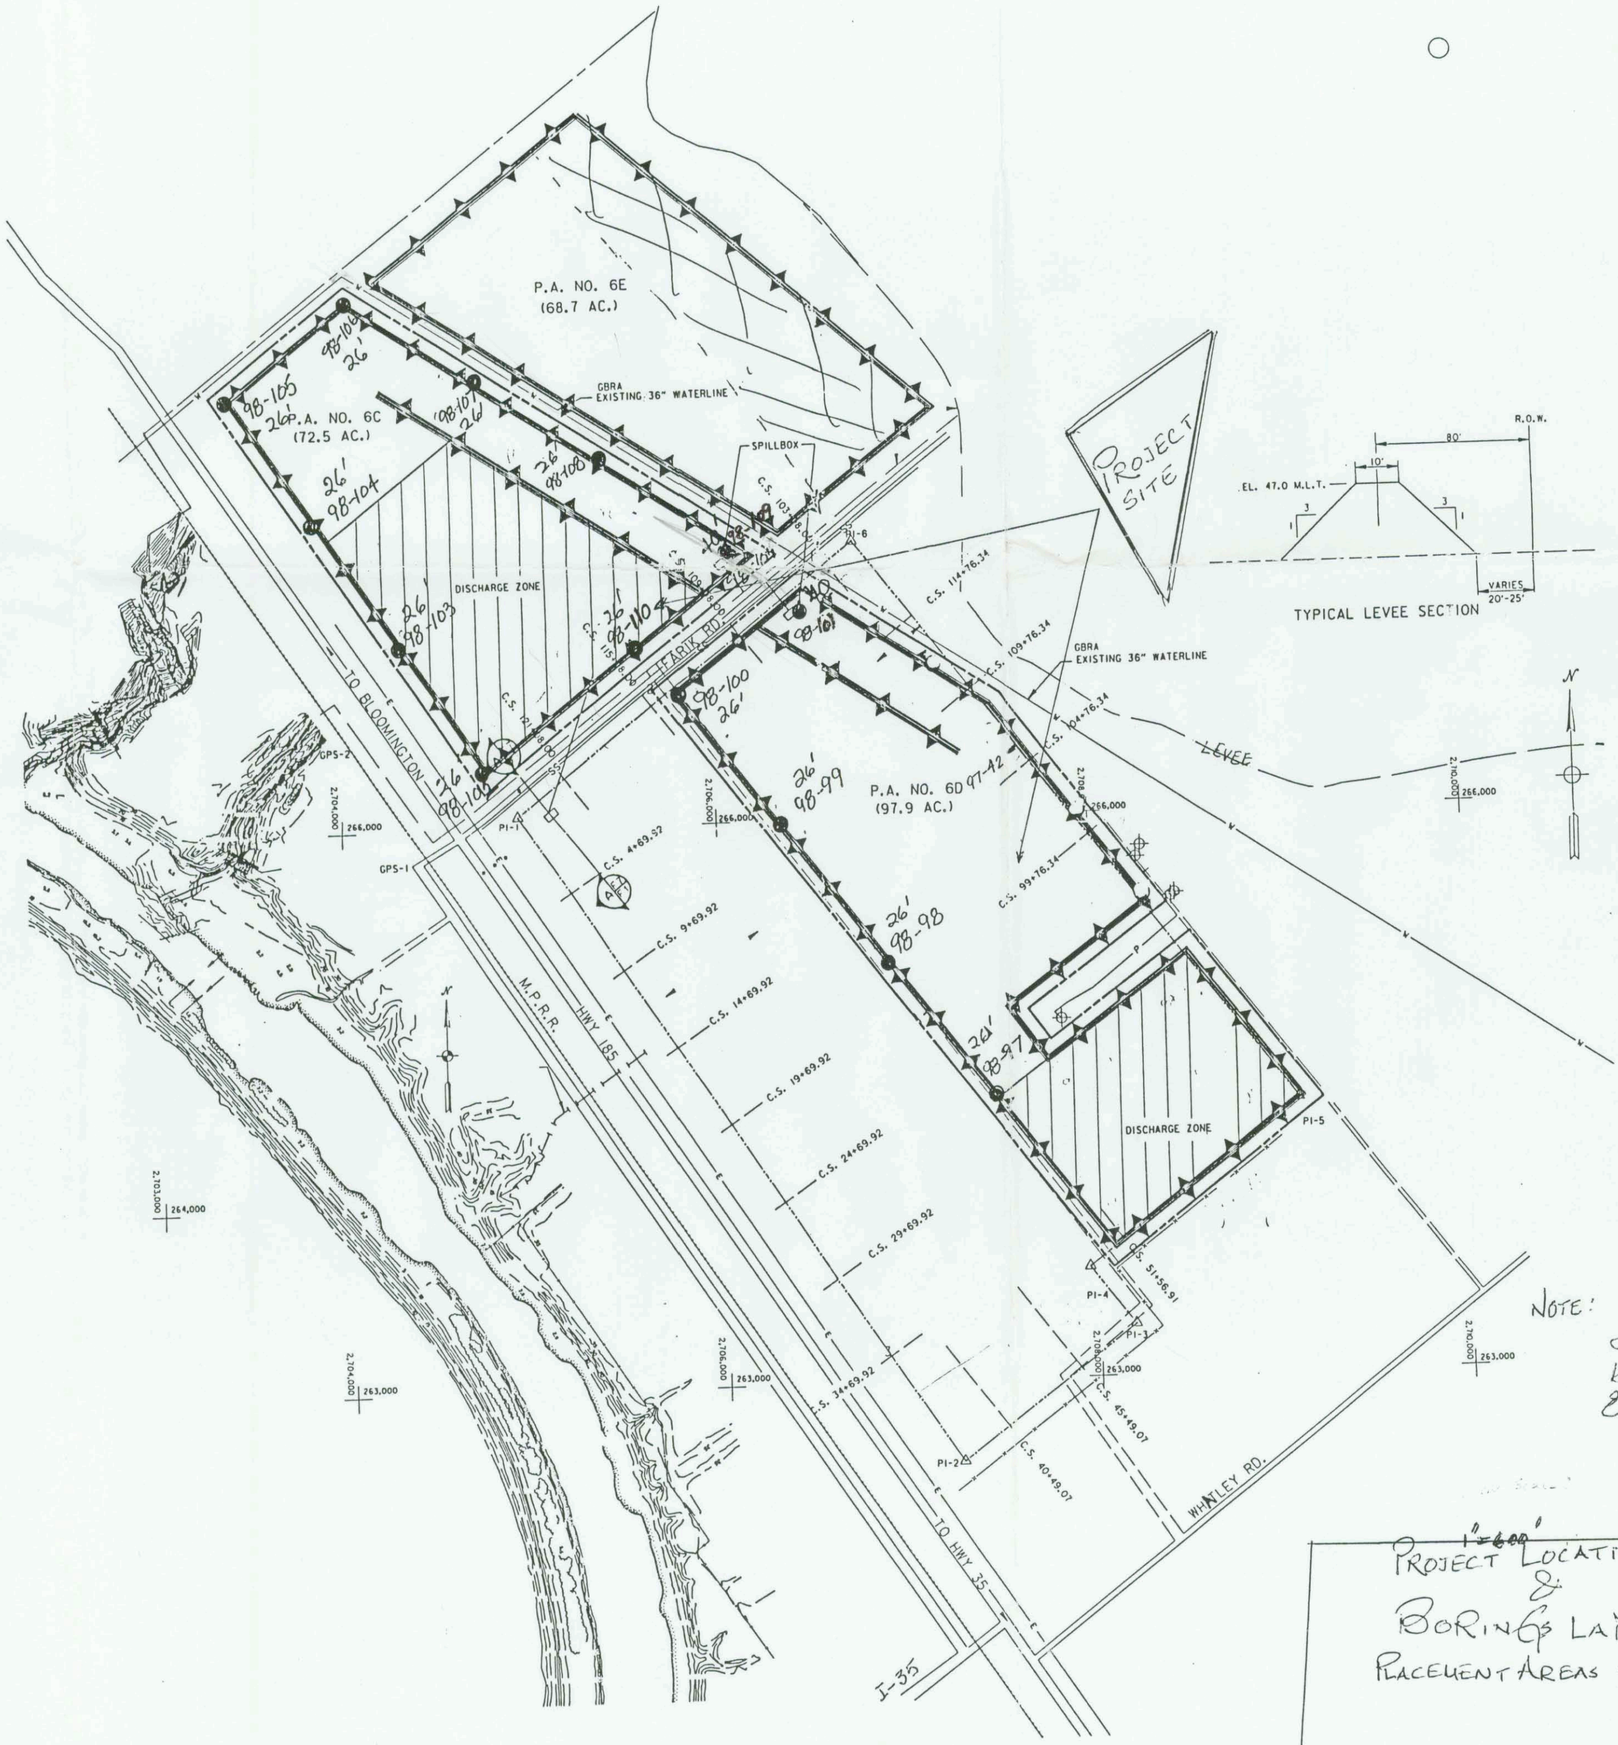

NOTE: All the borings shall be drilled to a depth 26' fee below the ground line EXCEPT Borings 98-101 & 98-109 shall be 40' fee deep.

1"=600'

PROJECT LOCATION MAP
&
BORING LAYOUT
PLACEMENT AREAS 6C & 6D.

FIG: 3
