U.S. ARMY CORPS OF ENGINEERS

BORING NO. 98-97 DATE: BEGIN 12-2-98 PAGE 1 / 1
JOB NO. 1140114801 COMPLETE 12-2-98 Thin Walled Tube
PROJECT Placement Areas NO. 6C and 6D ■ 3" □ 6"
LOCATION See plan of Borings
ELEVATION OF HOLE
MANUFACTURER'S DESIGNATION OF DRILL RIG Marsh Buggy F36
GROUNDWATER: DEPTH Dry ft., ELEV. ____ ft., at end of Drilling
WEATHER Foggy
DRILLER Dempsey Gearen LOGGER Jay Mostamand

DEPTH, FEET	SAMPLE	SAMPLE NO.	PEN./TORVANE SPT.-BLOW COUNT	COLOR	MATERIAL TYPE	CONSIS-TENCY	SECONDARY CONSTITUENTS	STRUCTURAL FEATURES AND COMMENTS
0		1	0.50	DK. gray	Clay	M. stiff		- w/roots
		2	0.75	DK. gray	Clay	M. stiff		- w/roots
5		3	1.00	DK. gray	Clay	stiff		- w/calc nod
		4	3.00	Yellowish Brown	Clay	V. stiff		- w/calc nod, Fer stains, SLKS
		5	3.25	Yellowish Brown	Clay	V. stiff		" " " " " "
10		6	3.25	Yellowish Brown	Clay	V. stiff		- w/calc nod, Fer stains, SLKS
		7	2.50	Yellowish Brown	Clay	V. stiff	Silty	- w/silt sms & silt layer
15		8		Yellowish Brown	Silt	M. Den.		
		9	2.75	Yellowish Brown	Clay	V. stiff		- w/silt sms, Fer stains, SLKS
		10	2.75	Yellowish Brown	Clay	V. stiff		- w/Fer stains, SLKS
20		11	2.75	Yellowish Brown	Clay	V. stiff		- w/Fer stains, SLKS
		12	2.75	Yellowish Brown	Clay	V. stiff		- w/Fer stains, SLKS
25		13	2.75	Yellowish Brown	Clay	V. stiff		- w/Fer stains, SLKS
30								
35								

GEOTEST ENGINEERING, INC.

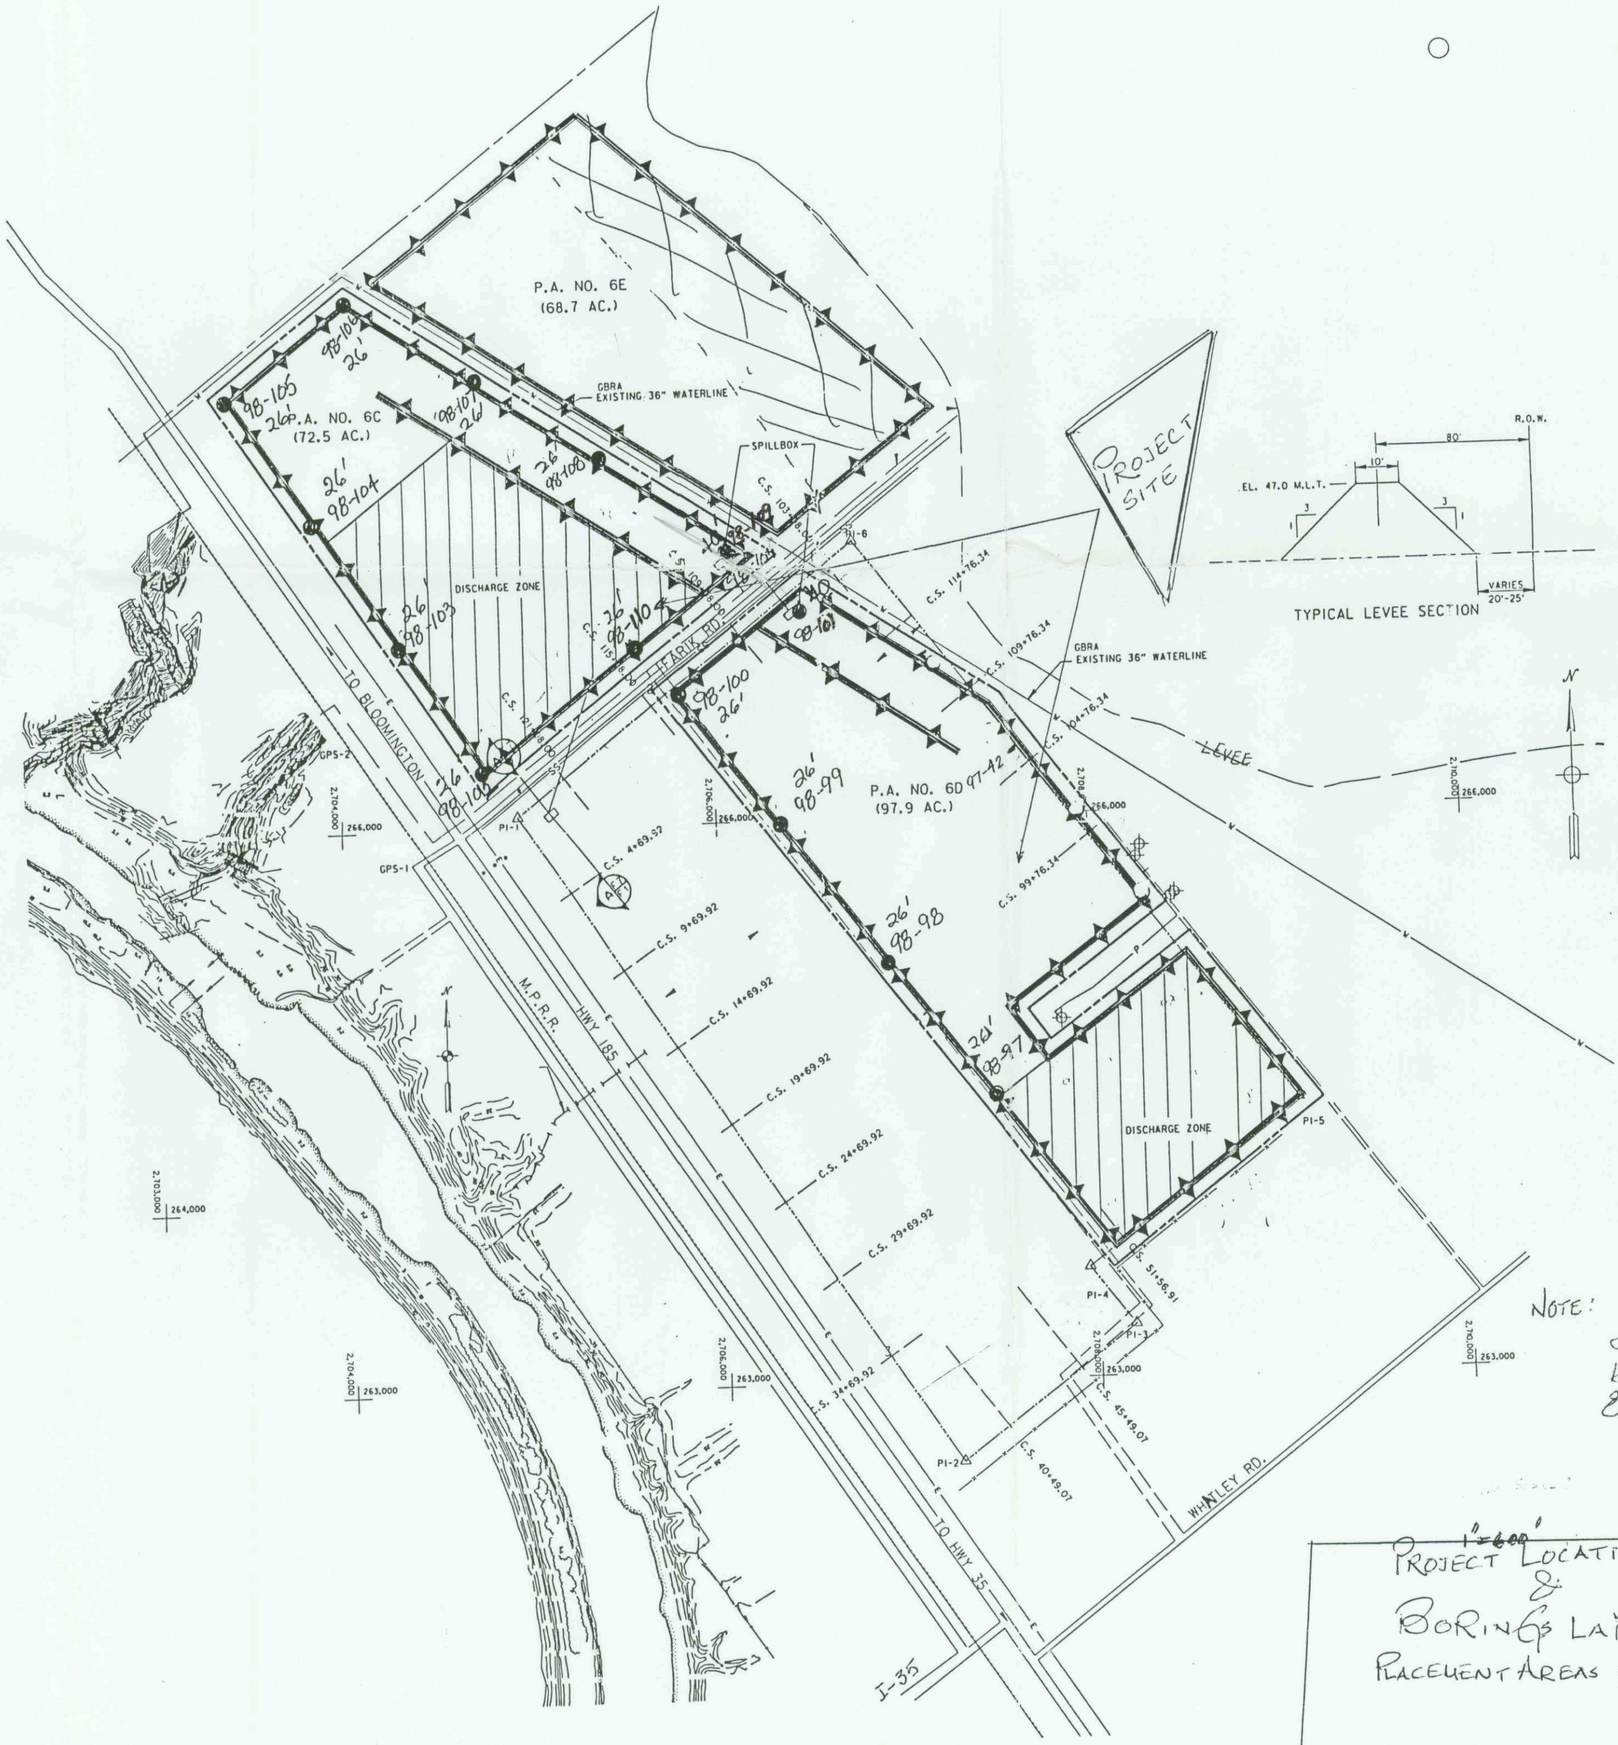

NOTE: All the borings shall be drilled to a depth 26' fee below the ground line EXCEPT Borings 98-101 & 98-109 shall be 40' fee deep.

1"=600'

PROJECT LOCATION MAP
&
BORING LAYOUT
PLACEMENT AREAS 6C & 6D.

FIG: 3
